

DW-GoM Start Work Checks: Demolition




DW-GoM Start Work Checks: Demolition

When to Complete – Before the start of any activities requiring **Demolition** of Equipment, Piping, or Tubing

All exposed person(s) performing work are to confirm each safeguard	How to examples:	Work Performer	Start-Work Verifier (OPS)
I HAVE CONFIRMED:		Initial	Initial
1 Equipment / Piping / Tubing to be demo'd is deinventoried / cleared of hazardous materials	(e.g. hydrocarbons, chemicals, contaminants, NORM, water, etc.)		
2 Safe Energy Isolation Start Work Check is complete	- Initialed by Work Performer and Start-Work Verifier - All energy sources are identified, isolated, and marked (e.g. electrical, pressure, gravity, etc.)		
3 Equipment / Piping / Tubing to be demo'd is tagged and marked per OPS-0140-PR01	3 tags should be present on the line each with a different signature (Operations – yellow, Team Lead – Green, Work Party – Purple) - Piping should have paint marking section to be removed - Tie-point flanges should also be identified		
4 Safe areas out of the line of fire are identified, with barriers in place where practical	- Area should be barricaded off - Identify if areas below cut need to also be barricaded		
5 Work area is assessed for potential dropped / unsecured objects, and potential objects have been removed or secured	Objects that may become loose / unsecure during the demolition process and have the potential to cause harm / damage		
6 Residual contaminants have been identified, and appropriate PPE / work methods established	(e.g. Mercury, lead, NORM, asbestos, hydrocarbons, chemicals, contaminants, PCB's, etc.)		
Confirm these controls/safeguards are in place and verified prior to starting work. Stop and seek help if anything changes.			

Verified By Print:	Verified By Sign:	Date:
-----------------------	----------------------	-------

UPD-GoM	OPS- 140: Piping and Tubing Demolition	
Aug 2023	Demolition Start Work Check	Rev 1.0
The controlled version of this "Business Control Document" resides online. Printed copies are UNCONTROLLED.		

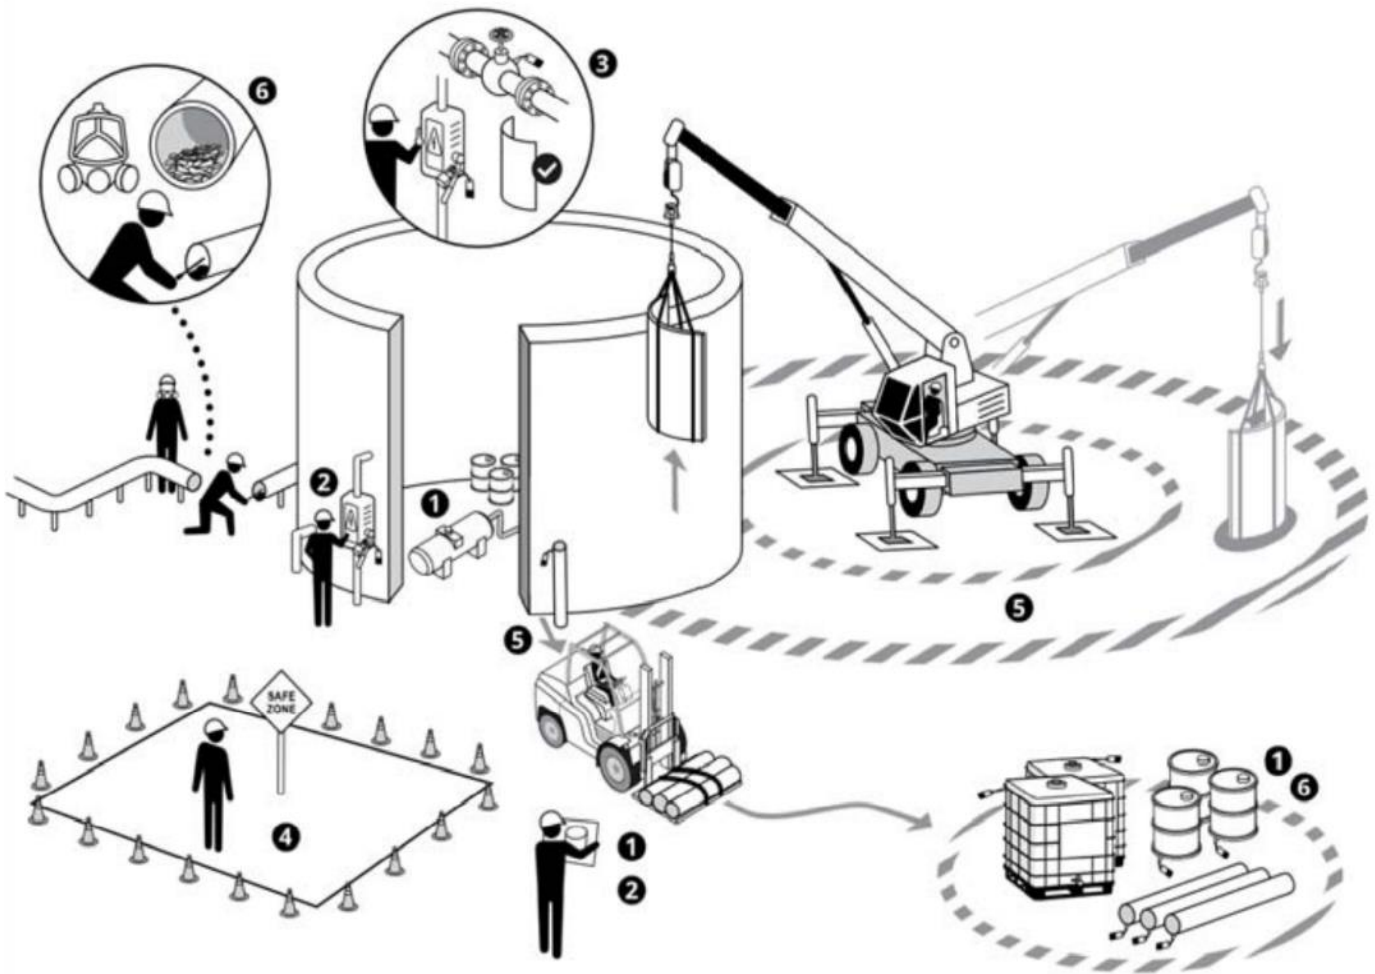

UPD-GoM	OPS- 140: Piping and Tubing Demolition	
Aug 2023	Demolition Start Work Check	Rev 1.0
The controlled version of this "Business Control Document" resides online. Printed copies are UNCONTROLLED.		
